



Installation Virtual Operations and Information Center (IVOIC)

Flood Control Update Brief

12 April 2011

Matt Barden
Chief, Plans & Operations

To provide the Army the installation capabilities and services to support expeditionary operations in a time of persistent conflict, and to provide a quality of life for Soldiers and Families commensurate with their service.

We are the Army's home

Jeremiah Cowgill
Emergency Manager
IVOIC / EOC

(309) 782-4573 / DSN 793-4573
ROCK-EOC@conus.army.mil

UNCLASSIFIED

Flood Control Update Brief



IMCOM
SOLDIERS • FAMILIES • CIVILIANS



AGENDA

- I. Purpose
- II. Safety Message
- III. SITREP (Updated)**
- IV. National Weather Service Flood Predictions (a/o 25 Mar 11) (Updated)**
- V. Flood Build-Up (Updated)**
- VI. SIGACTS
- VII. River Stage, Forecast, and Water Elevation (Updated)**
- VIII. Public Affairs Summary / Photos
- IX. Community Links (Updated)**
- X. Road Closures (New Slides)**
- XI. RFIs

UNCLASSIFIED

Flood Control Update Brief



Purpose:

To inform the tenants of Rock Island Arsenal of the impending flood and provide a timely and comprehensive flood status update.

Flood Control Update Brief



IMCOM
SOLDIERS • FAMILIES • CIVILIANS



In preparation for the forecasted flood, crews will begin erecting a flood wall on top of the north levee from Gillespie Street to the east end of the Island.

As this operation begins, this area will be designated as a restricted area, barricaded, and only be used by security and personnel working the flood situation.

We appreciate everyone respecting the designated restricted area and not walking, jogging, or driving in these areas. As the river level rises, additional areas will become restricted.

UNCLASSIFIED

Flood Control Update Brief



SITREP a/o 12 Apr 11

As of now the flood forecast through Apr 19th shows moderate flooding occurring and rising above major flood stage to 18.7' by Apr 19th. The increase in flood stage is a result of snow melt and rain fall that occurred to the north over the weekend. The Mississippi river is expected to continue to respond to the remaining snow melt until late April. Preparedness/Mitigation updates are as follows:

1. Current flood prediction for the next week do not warrant any further Hesco installations at this time.
2. Delivery of bulk sand completed.
3. Continuing to install rip rap on the water side of the north levee to protect from erosion.
4. Continuing to monitor flood predictions.
5. Planning medical vaccinations for DPW staff next week with medical clinic.

UNCLASSIFIED

Flood Control Update Brief


NWS Flood Predictions



IMCOM
SOLDIERS • FAMILIES • CIVILIANS



1 Week Chances of Exceeding River Levels on the MISSISSIPPI R at QUAD CITIES
Latitude: 41.3 Longitude: 98.4
Forecast for the period 3/30/2011 - 6/22/2011
This is a conditional simulation based on the current conditions as of 3/23/2011

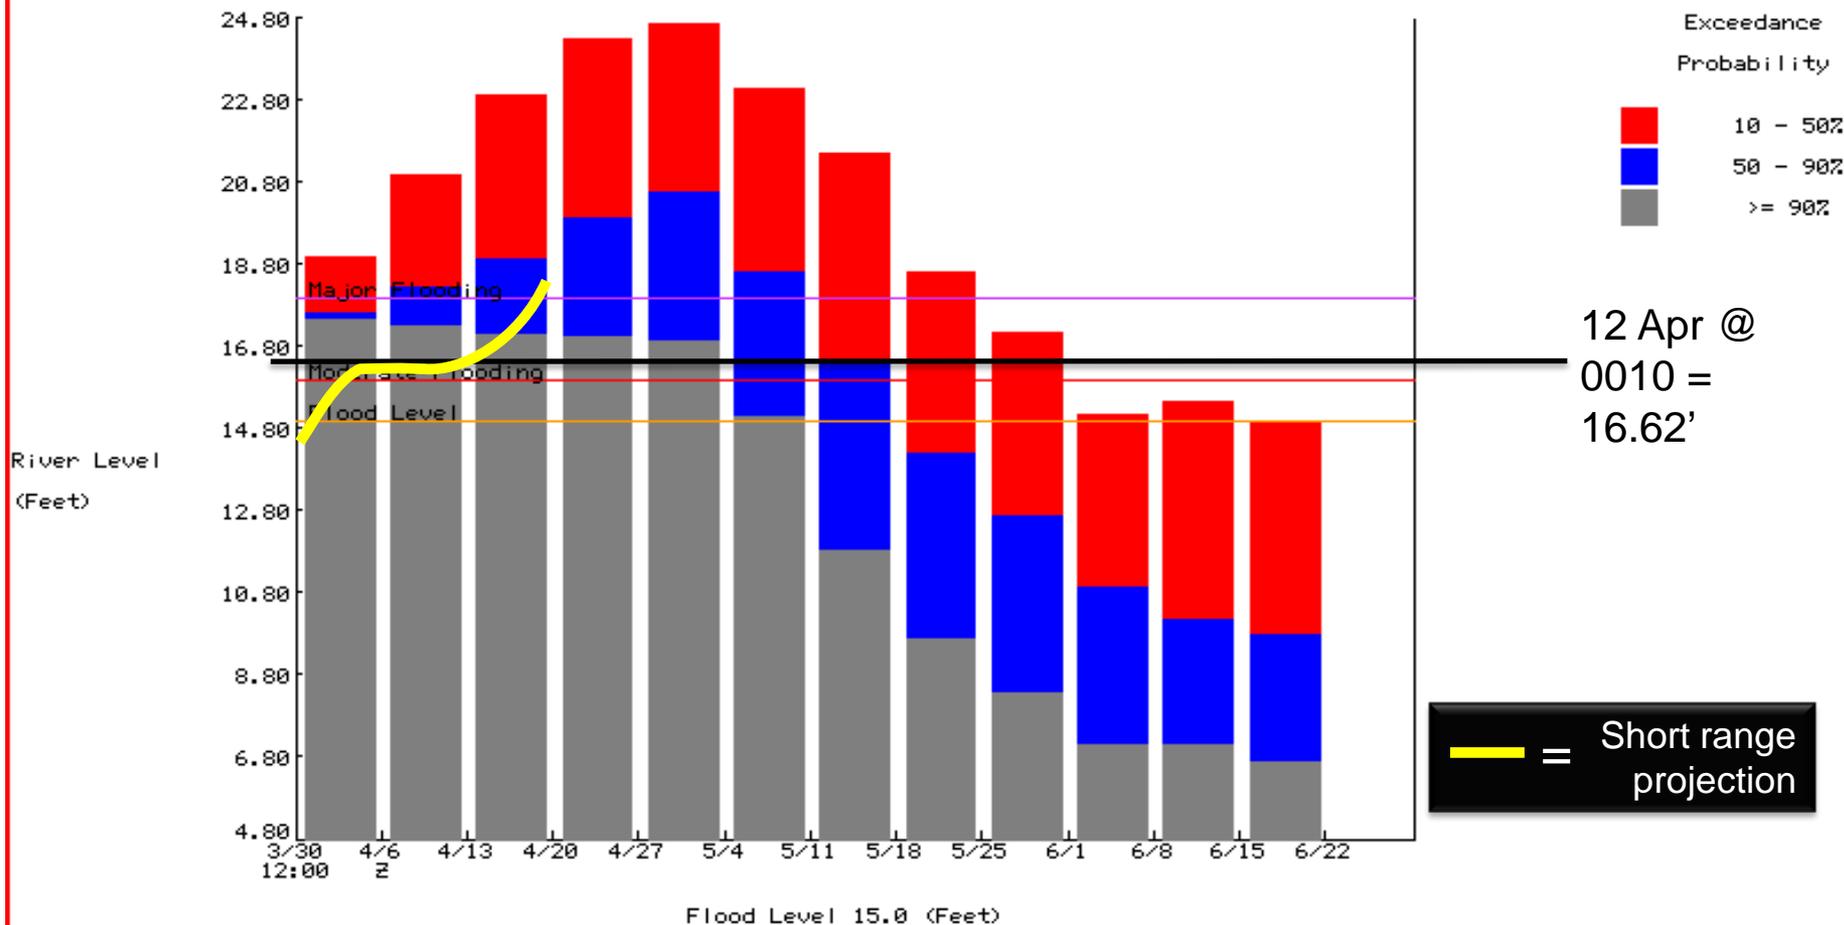

12 Apr @
0010 =
16.62'

— = Short range projection

UNCLASSIFIED

Flood Control Update Brief



IMCOM
SOLDIERS • FAMILIES • CIVILIANS




Flood Build-Up (2011)

Flood Exceedance Probability
 50 – 90%
 10 – 50%

12 Apr = 16.62'
 @ 0010
 + .1 from 11 Apr

Flood of Record = 22.63'

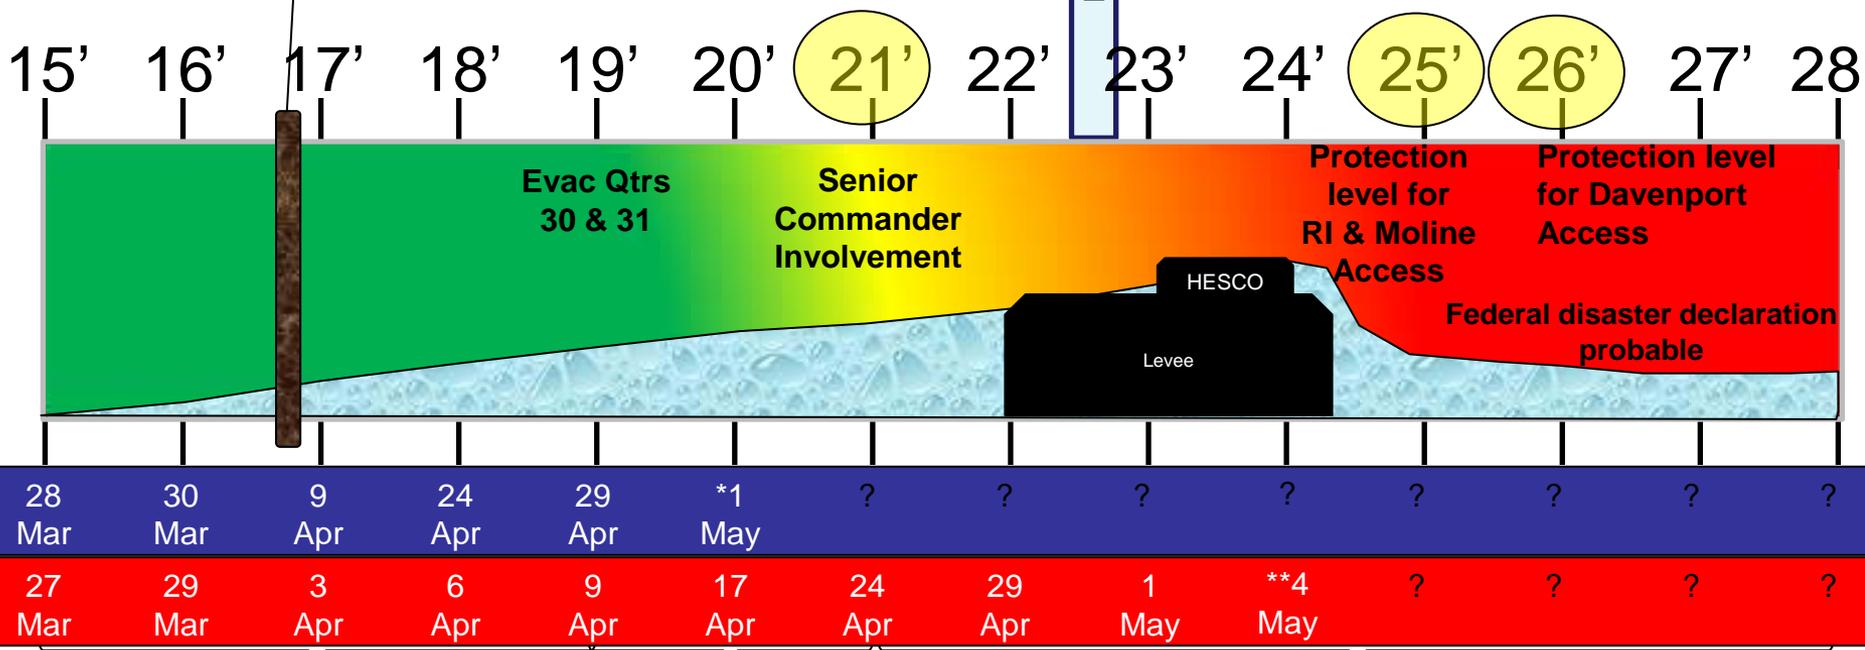

- Plan
- Install sandbags & Hescos
- Train Levee teams
- Coordinate
- Operate RIAG EOC

- Operate DPW ICC
- Inspect levees
- Increase STRATCOM
- Plan/coordinate

- Operate DPW ICC/RIAG EOC 24/7
- Inspect levees 24/7
- Increase communications with community
- MDMP/Plan COOP & Evacuation

UNCLASSIFIED



Severe Weather Update Brief



IMCOM
SOLDIERS • FAMILIES • CIVILIANS



SIGACTs

Date / Time	SIGACTS
24 MAR / 0800	Flood Control Planning Meeting - Initial meeting
25 MAR / 0800	CG Brief
27 MAR / n/a	Sandbag fill complete (45K)
29 MAR / 0900	Soldier Training (Classroom – Medical, Commo, Safety, Ops)
(Postponed)	Training for Soldiers (Levee Patrol and Ops during Flood Fighting)

UNCLASSIFIED


Flood Control Update Brief



IMCOM
SOLDIERS • FAMILIES • CIVILIANS



Weekly Forecast (a/o 12 Apr 11)

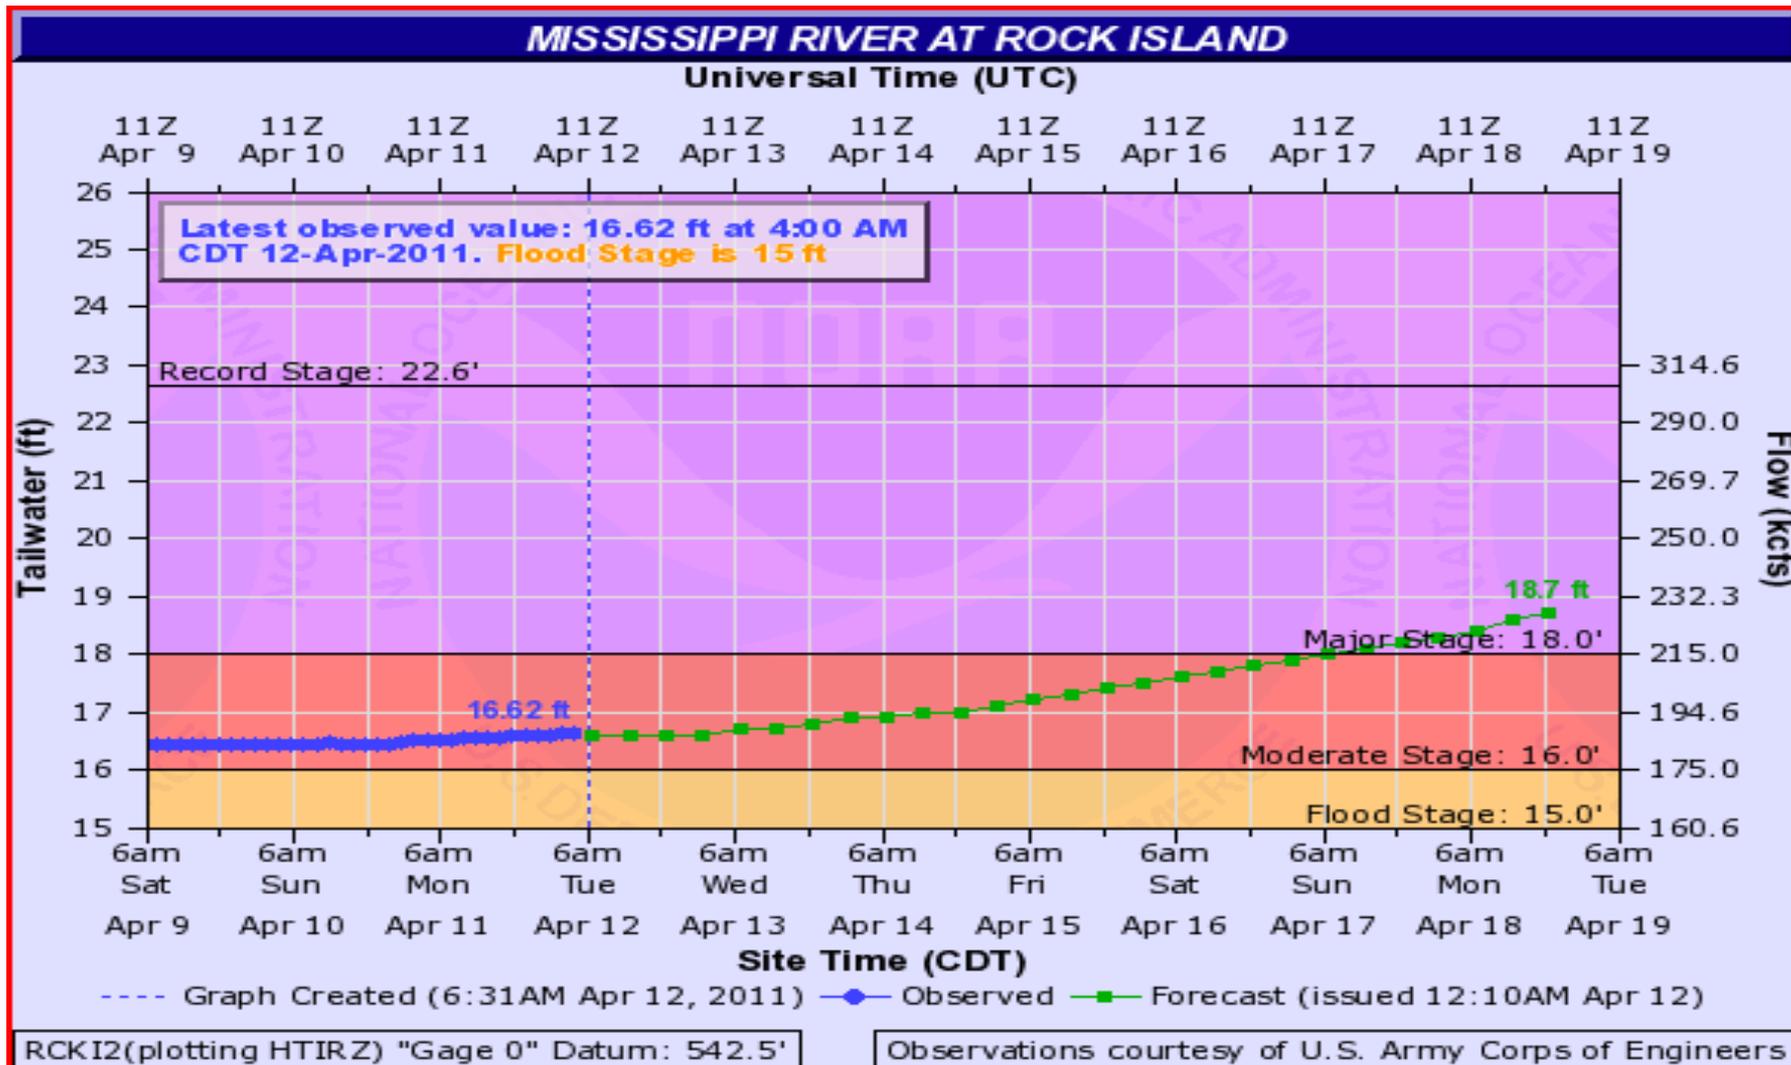

UNCLASSIFIED

Flood Control Update Brief



Public Affairs Summary

Current Ops

- Flood website w/FAQs being developed. http://public-dev.ria.army.mil/sites/flood_information/
- DPTMS interview that aired on WHBF TV4: <http://bit.ly/hswg5v>
- Continue to take photos for historic reference.

Future Ops

- TBD

Assessments

- TBD



Same photos as
31 Mar 11



Flood Control Update Brief



IMCOM
SOLDIERS • FAMILIES • CIVILIANS



Community Links

City:

[East Moline](#)

[Moline](#)

[Bettendorf](#)

[Rock Island](#)

[Davenport](#)

County:

[Scott County EMA](#)

[Rock Island County EMA](#)

Additional Links:

[Map for RIA Flood Plan](#) (NEW on 1 Apr 11)

[Davenport Library Info](#)

[USACE Rock Island District](#)

[River levels](#)

[FEMA widget](#)

[Community Flood Watch Video](#)

In the News:

[Mississippi expected to top 19 feet next week & High water, road work create detours](#) - Courtesy of QC Times (NEW on 12 Apr 11)

UNCLASSIFIED

Flood Control Update Brief



Area Road Closures Due to Flooding

Iowa

Davenport:

- [South Concord Street from Miller to Wapello avenue closed because of water over the road in the area just west of the Waste Water Treatment Plant drive.](#)
- [Biederbecke Drive at Main Street in downtown Davenport has been closed for construction of a dike across street.](#)
- [East River Drive from East 4th St. to Brady Street has been closed due to flooding.](#)

Bettendorf: none

Illinois

Rock Island:

Moline:

- [River Drive from 34th st to 55th st](#)

East Moline:

RIA

None

Flood Control Update Brief



IMCOM
SOLDIERS • FAMILIES • CIVILIANS



RFIs

1. Should the flood waters reach such a level to constrain (but not totally prohibit) traffic onto RIA and tenant mission performance; how will the guard force implement further access control limits to only allow entrance of those authorized by each tenant for high priority MEFs?
 - As of now we currently don't have MEF rosters built into the RCx (the vetting system used for access control). We have the capability to build rosters into the system but it becomes a matter of maintaining rosters and pushing updates to the DES for the RCx system. This is an issue that will require further analysis from COOP planners on the installation and the DPTMS & DES.

UNCLASSIFIED

Flood Control Update Brief



IMCOM
SOLDIERS • FAMILIES • CIVILIANS



End of Brief

INSTALLATION MANAGEMENT COMMAND



IMCOM
SOLDIERS • FAMILIES • CIVILIANS

“Sustain, Support and Defend”

UNCLASSIFIED
